

12 December 2009


Dear Resident or Business Occupier



York Place and Broughton Street Tram works - January 2010

We are committed to providing you with as much information as possible about the plans for work in your area and would like to take this opportunity to thank you for the patience and understanding you have shown during what we know has been a period of disturbance. As a thank you to the City, all major tram works in your area have halted until the New Year.

From Monday, 4 January we will recommence tram works on York Place. The map below shows the areas where we will be working and the signed traffic management which will be installed.

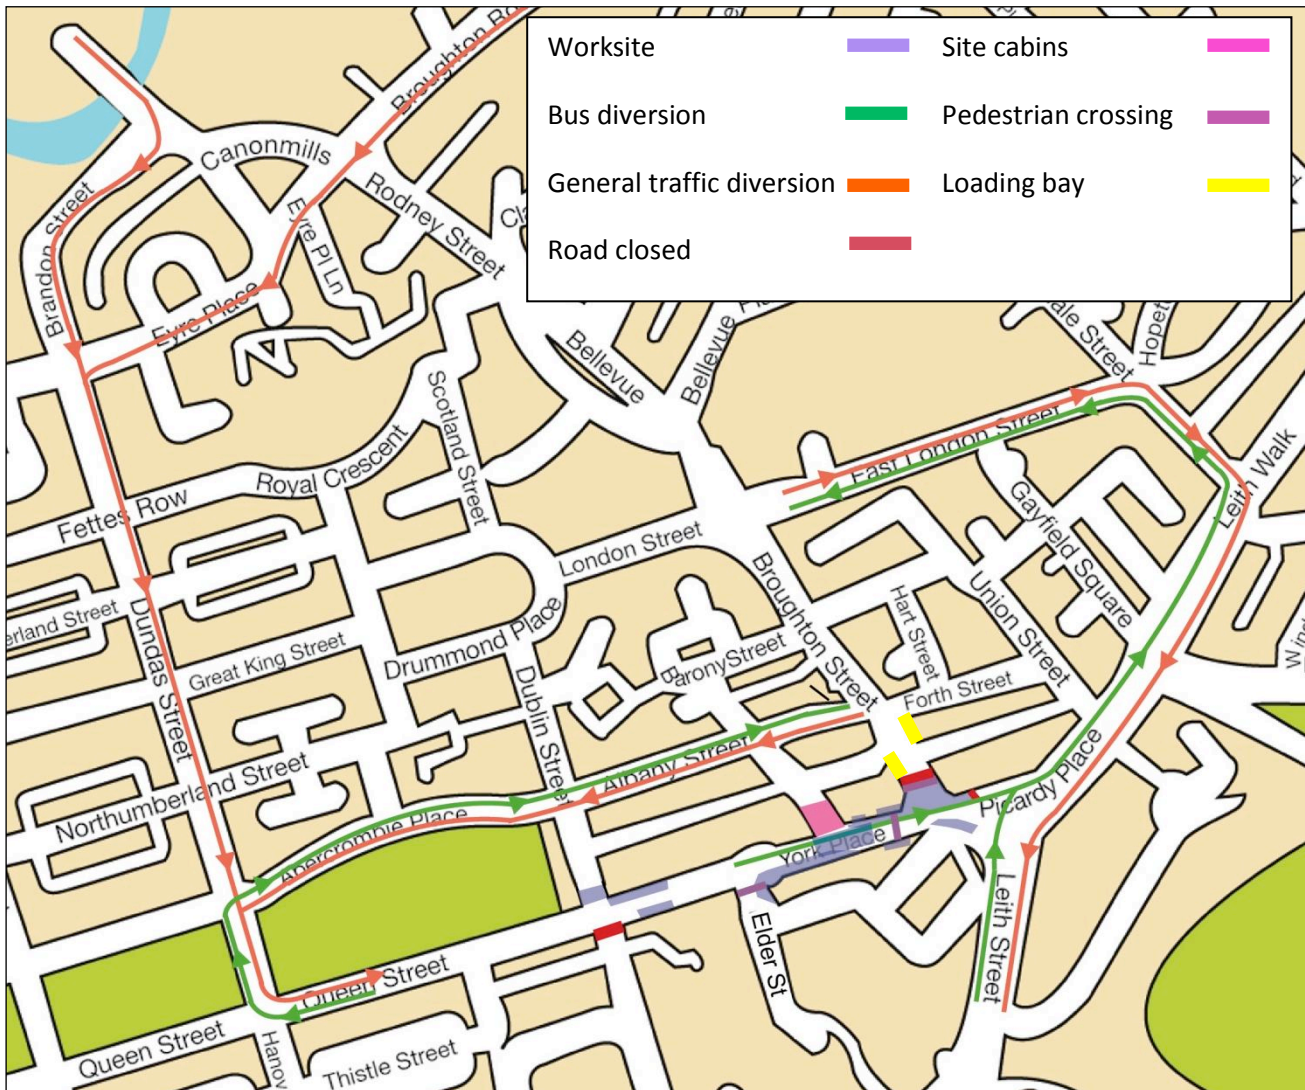

Please see the table overleaf for more information about these worksites.


For more information about our other works please visit www.edinburghtrams.com and click on **My Local Updates**. Alternatively, you can call our Customer Helpline on 0800 328 3934 or email info@edinburghtrams.com

Yours faithfully

Steven Bell, Tram Project Director

Find out more about Edinburgh Trams online



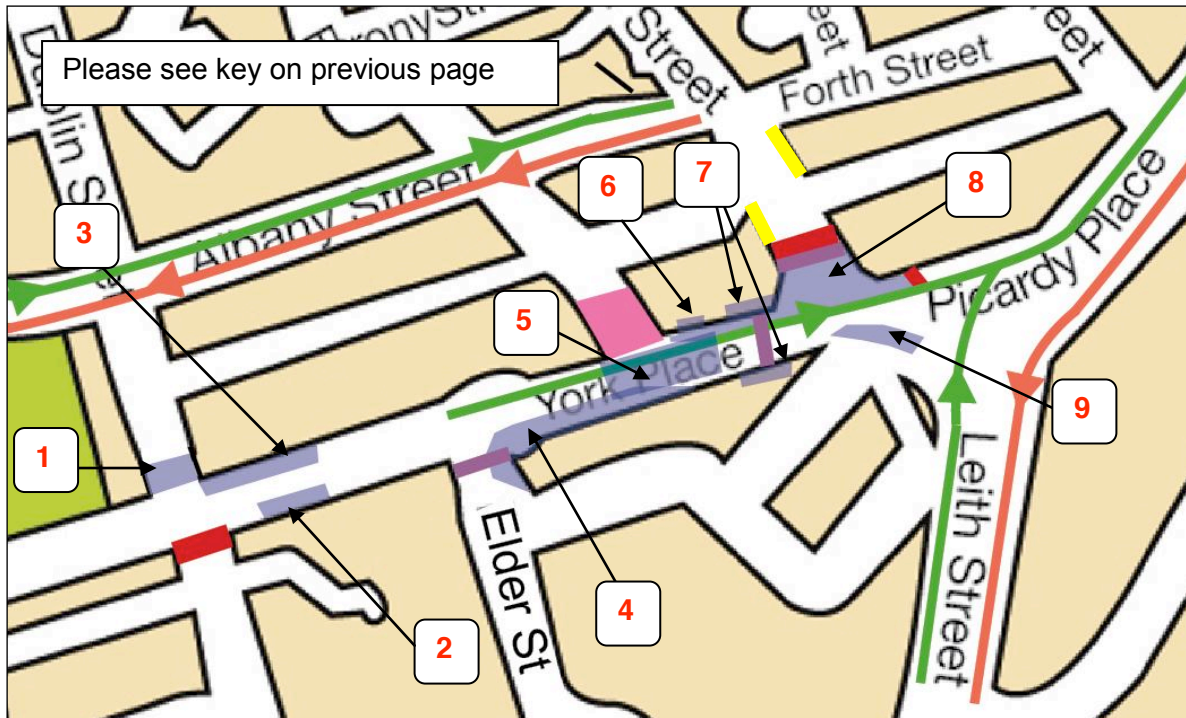

Site	Start Date	Description	Duration
1	4 January	Enabling work at the junction of Dublin Street and York Place to prepare for the opening of Dublin Street to traffic. <ul style="list-style-type: none"> • Dublin Street will be open to left in, left out traffic from 9 January while Broughton Street is closed • Road markings painted and signs erected to show reduced speed limit (20mph) 	9 January
2	Mid January	Worksite installed on the south side of York Place, east of North St Andrew Street.	End January
3	Mid January	Worksite installed on the north side of York Place, east of Dublin Street	Mid February
4	4 January	Worksite installed on the south side of York Place and into Elder Street. <ul style="list-style-type: none"> • Pedestrian crossing across York Place will be closed • East/west pedestrian crossing on Elder Street will remain operational • Left hand turn into Elder Street will be maintained 	End January
5	Late January	Worksite installed in the centre of York Place. <ul style="list-style-type: none"> • Two way traffic maintained around the site 	End Feb
6	4 January	Worksite on the north footpath near St Paul's and St George's Church. <ul style="list-style-type: none"> • Pedestrian footpath maintained 	Mid Feb
7	4 January	Sites installed on both sides of the road to allow the installation of a temporary pedestrian crossing.	One week
8	9 January	Worksite installed at Broughton Street and extending westwards on the carriageway to York Place Lane. <ul style="list-style-type: none"> • Broughton Street will be closed to through traffic • Local access maintained • Some parking restrictions to allow for Business loading • Dublin Street will open to left in and left out traffic while Broughton St is closed • Dublin Street will have a 20mph limit • The pedestrian crossing facilities across York Place will be maintained • An eastbound bus stop will be maintained at this location • The west end of Picardy Place will be closed to traffic, access maintained via the east end 	Mid February
9	9 January	Two days work to remove the traffic and pedestrian island at the east end of York Place. This will enable traffic lanes to move during construction.	10 January

